| Line | Name | Duration | Start | Finish |
|---|---|---|---|---|
| 1 | **SUB-CONTRACTOR APPOINTMENT** | **294d** | **10/08/15** | **14/10/16** |
| 2 | Window Installer | 11w 4d | 10/08/15 | 06/11/15 |
| 3 | Scaffolding | 10w 4d | 10/08/15 | 30/10/15 |
| 4 | Temporary Services | 6w 4d | 17/08/15 | 12/10/15 |
| 5 | Temporary Accomodation | 5w 4d | 24/08/15 | 09/10/15 |
| 6 | General Attendance | 5w | 28/08/15 | 09/10/15 |
| 7 | Sub-structure | 12w | 07/09/15 | 04/12/15 |
| 8 | Carpentry & Joinery | 12w | 07/09/15 | 04/12/15 |
| 9 | Architectural Metalwork | 12w | 14/09/15 | 11/12/15 |
| 10 | General Builder | 12w | 02/11/15 | 12/02/16 |
| 11 | Soft Strip | 9w | 02/11/15 | 22/01/16 |
| 12 | Mechanical & Electrical Services | 12w | 23/11/15 | 04/03/16 |
| 13 | Kitchen Fit Out | 11w | 30/11/15 | 04/03/16 |
| 14 | Roof works | 11w 2d | 29/02/16 | 27/05/16 |
| 15 | Landscaping | 12w 1d | 07/03/16 | 10/06/16 |
| 16 | Stone & Tiling | 10w 3d | 29/03/16 | 17/06/16 |
| 17 | Hardwood Floors | 8w 3d | 25/04/16 | 01/07/16 |
| 18 | Audio & Visual | 11w | 31/05/16 | 19/08/16 |
| 19 | Painting & Decorating | 11w | 06/06/16 | 26/08/16 |
| 20 | Floor Finishes | 7w 4d | 25/07/16 | 23/09/16 |
| 21 | Builder Clean | 6w 4d | 22/08/16 | 14/10/16 |
| **22** | **LONG LEAD ITEMS** | **240d** | **09/11/15** | **28/10/16** |
| 23 | Windows | 17w | 09/11/15 | 18/03/16 |
| 24 | Frames & Doors | 15w 3d | 07/12/15 | 08/04/16 |
| 25 | Metal Stairs | 21w 2d | 14/12/15 | 27/05/16 |
| 26 | Special bricks | 12w | 14/12/15 | 18/03/16 |
| 27 | Slates | 13w 2d | 22/02/16 | 27/05/16 |
| 28 | Timber Stairs | 17w | 01/03/16 | 01/07/16 |
| 29 | Boilers | 9w 2d | 07/03/16 | 13/05/16 |
| 30 | Fire Alarm Panel | 9w 2d | 07/03/16 | 13/05/16 |
| 31 | Security Panel | 9w 2d | 07/03/16 | 13/05/16 |
| 32 | Kitchen | 18w 1d | 07/03/16 | 15/07/16 |
| 33 | Sanitaryware Schedule | 16w 1d | 13/04/16 | 05/08/16 |
| 34 | Stone worktop | 9w 4d | 09/05/16 | 15/07/16 |
| 35 | Lights - Type A | 11w 4d | 16/05/16 | 05/08/16 |
| 36 | Special radiators | 11w 4d | 16/05/16 | 05/08/16 |
| 37 | Fire place | 11w 4d | 16/05/16 | 05/08/16 |
| 38 | Cupboards | 14w 3d | 23/05/16 | 02/09/16 |
| 39 | Vanity Units | 14w 3d | 23/05/16 | 02/09/16 |
| 40 | Stone floor - Type A | 13w 4d | 20/06/16 | 23/09/16 |
| 41 | Timber floor | 11w 4d | 04/07/16 | 23/09/16 |
| 42 | LED TV's | 9w 4d | 22/08/16 | 28/10/16 |

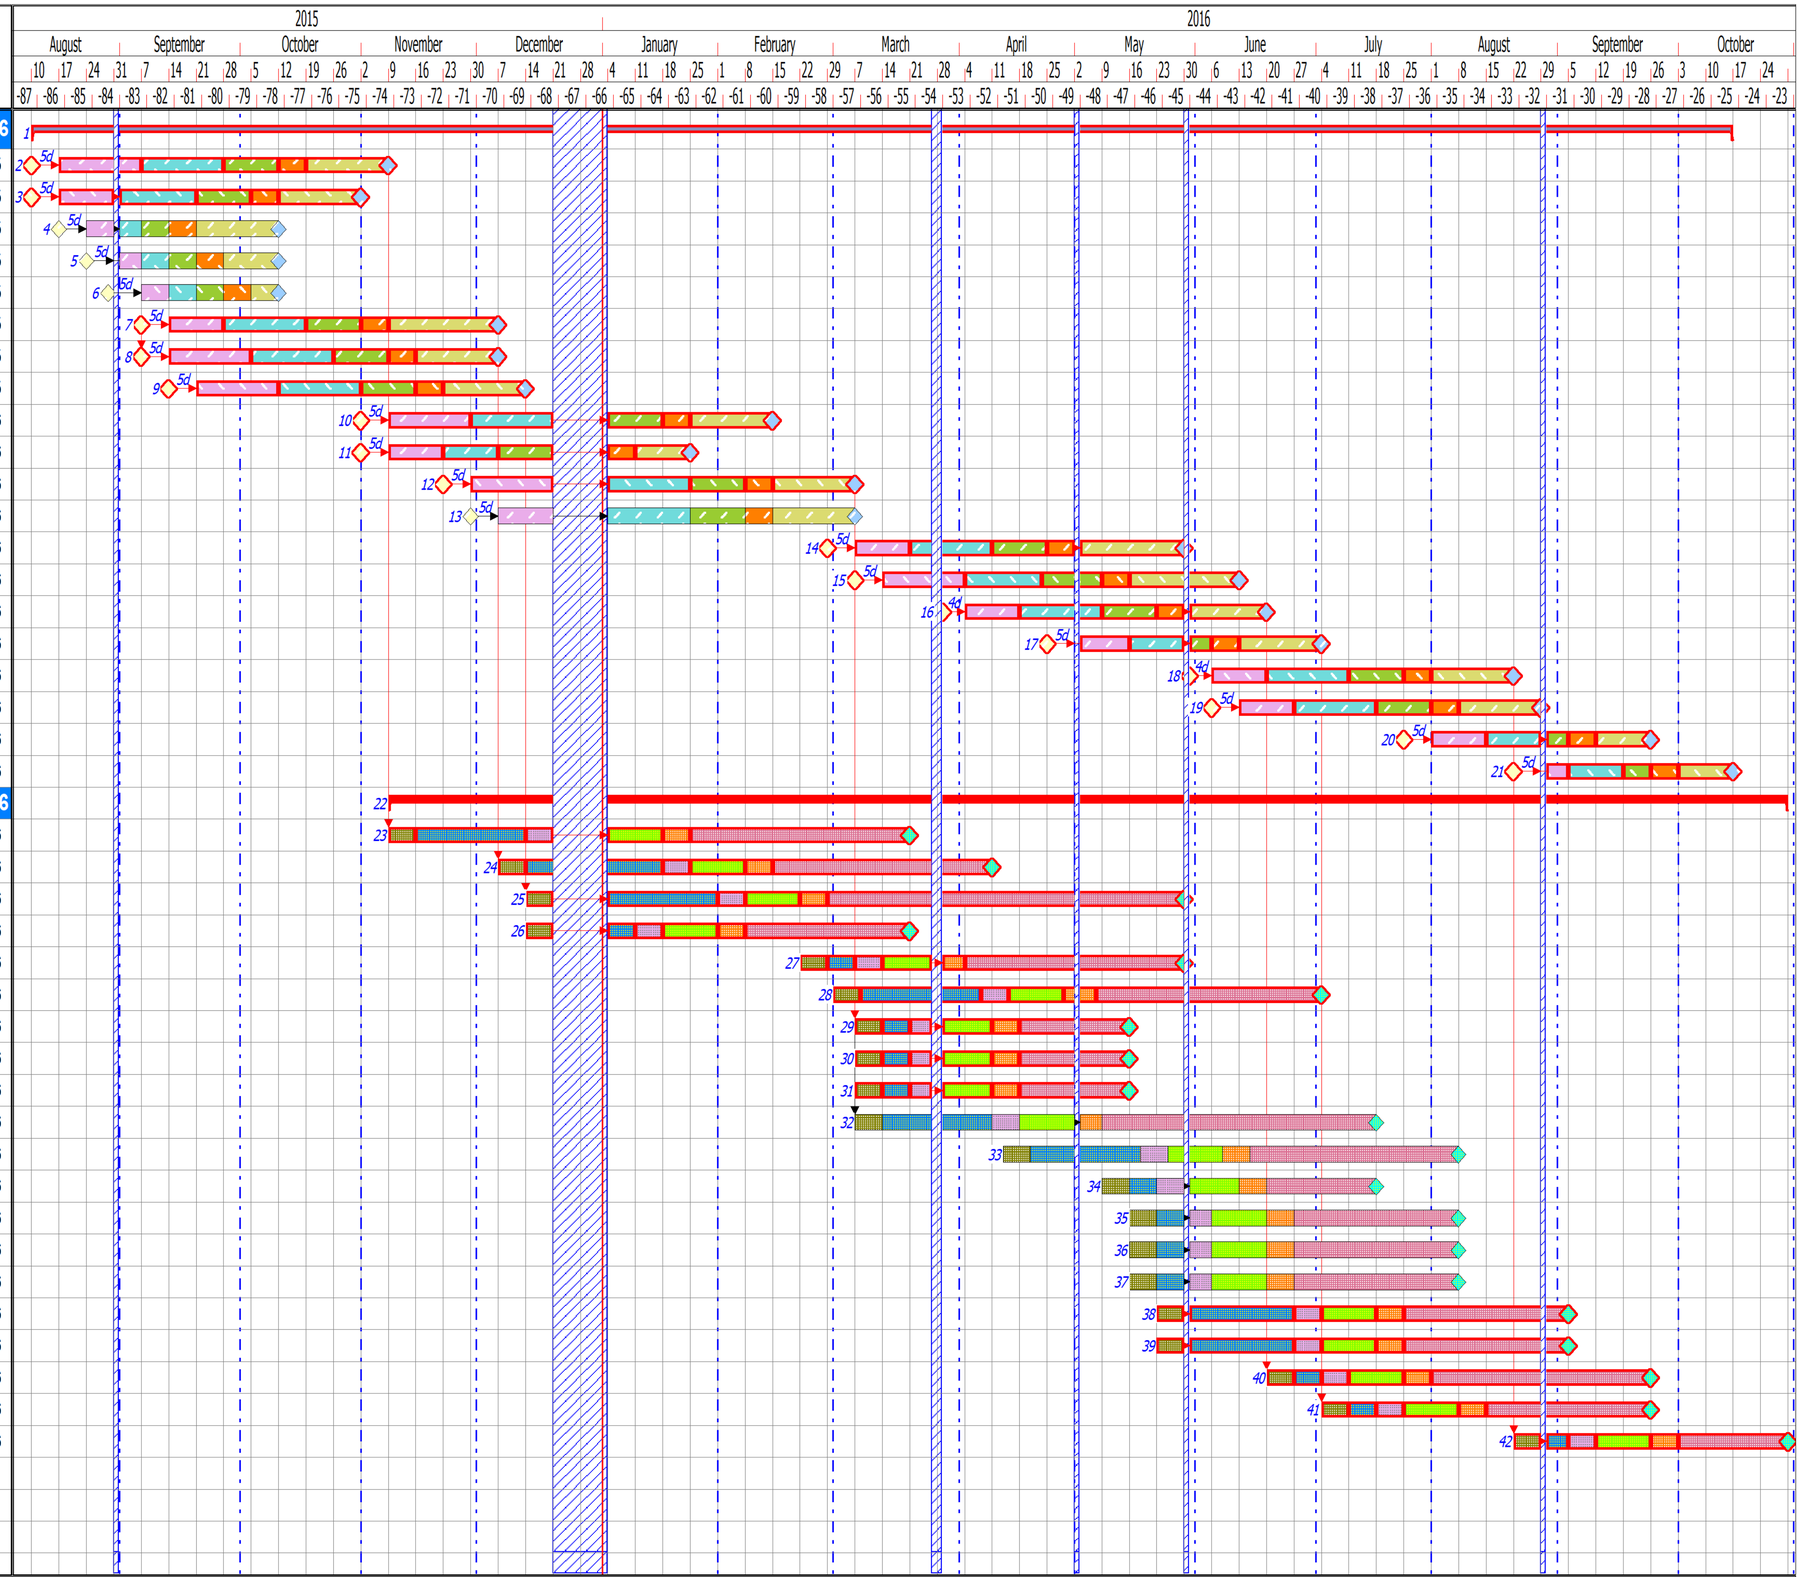


Project Codes

- Contractor Appointments
- Issue samples/drawings for approval
- Long Leads
- Evaluate
- Agree Tender List
- Status sample/drawings
- Review Design
- Approve
- Prepare Tender Documents
- Place order
- Mobilisation
- Dwgs/TS/Samples
- Manufacture
- Tender
- Start
- Arrive on site

Planned by Asta Powerproject
